OCKFORD RIDGE NEW BUILD & REFURBISHMENT PROGRAMME

Andrew Smith and Louisa Blundell





History of Ockford Ridge

- Land purchased from Eashing Park
 Estate and Godalming Burial Ground
- Building commenced 1930 1931
- First residents moved in September
 1931





Project Inception

• July 2012

Council approved Affordable Homes Delivery Plan 2012 – 2017

February 2013

Housing Delivery Board established

March 2013

Proposals for remodelling and redevelopment of Ockford Ridge



Pre-development

April 2013

Framework for the purchase of land or property

June / July 2013
 Consultation

December 2013

Proposals for remodelling and redevelopment of Ockford Ridge



Planning

- August 2014 Hybrid planning application
- March 2015 Full application for development of two show homes
- April 2016 Site compound
- January 2017 Site A planning application submitted



Current position

Redevelopment
 Sites A, B, C and D





Site D


















Show homes





Current position

Refurbishment
 Pilot Phase
 Phases 1 - 3

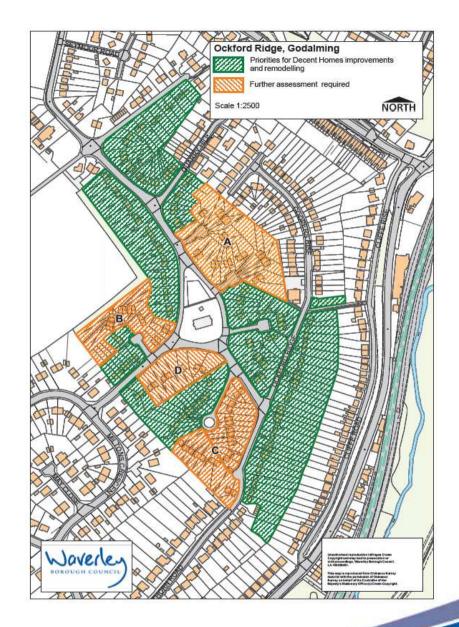



Governance and Community Involvement

- Executive & Council
- Housing Delivery Board
- Ockford Ridge Programme Group
- Ockford Ridge Community Consultative Group
- Ockford Ridge Community Initiative Group



Procurement & Budget – current & future years

	2017/18		2018/19	2019/20	Total
	Budget	Requested rescheduling to 17/18 (to be approved 11.07.2017 exec)	Budget	Budget	
New Build					
Show Homes	12,150			152,860	165,010
Site A	4,628,440		5,024,080	256,910	9,909,430
Site D	1,504,740		1,800,000		3,304,740
Site B		60,398	121 111		60,398
Site C	- 8	80,504	30		80,504
Utility/Highways works	N .	1,418,275	750,000		2,168,275
Total New Build Budget	6,145,330	1,559,177	7,574,080	409,770	15,688,357

	2017/18		2018/19	2019/20	Total
	Budget	Requested rescheduling to 17/18 (to be approved 11.07.2017 exec)	Budget	Budget	
Refurbishment					
Pilot Phase		155,368			155,368
Phase 1		750,839			750,839
Phase 2	1,115,000	72,928			1,187,928
Phase 3		*	485,000		485,000
Further Phases	- F	682,569	8	3,750,000	4,432,569
Total Refurbishment Budget	1,115,000	1,661,704	485,000	3,750,000	7,011,704
Total Budget	7,260,330	3,220,881	8,059,080	4,159,770	22,700,061



Next steps

Summer 2017

Community 'meet contractor event'
Surveys for next refurbishment phase
Work to bring forward site B
Site D start on site
Planning permission granted Site A
Communications continue through Newsletters
/ further drop in events



Development Team – Role in Ockford Ridge Project

Name	Role
Andrew Smith	Strategic Management
Louisa Blundell	Day to day management Refurbishment programme
Mark Constable	Delivery of site A Bring forward Site C
Irina Seriogina	Delivery of site D
Mark Orosz	Delivery of site B
Fiona Stewart	Tenant Liaison Officer
